



Funded by
the European Union

HORIZON EUROPE PROGRAMME – TOPIC: HORIZON-CL5-2022-D5-01-02



AENEAS

innovAtive ENERgy storage systems onboArd vessels

Deliverable D 8.1

Project management handbook



Deliverable Type	Report
Dissemination Level	Sensitive
Due Date (Annex I)	30.04.2023 (Month 3)
Pages	23
Document Version	Final
GA Number	101095902
Project Coordinator	Mohsen Akbarzadeh Flanders Make (FM) (Mohsen.Akbarzadeh@flandersmake.be)

LEGAL DISCLAIMER

Copyright ©, all rights reserved. No part of this report may be used, reproduced and or/disclosed, in any form or by any means without the prior written permission of AENEAS and the AENEAS Consortium. Persons wishing to use the contents of this study (in whole or in part) for purposes other than their personal use are invited to submit a written request to the project coordinator.

The authors of this document have taken any available measure in order for its content to be accurate, consistent and lawful. However, neither the project consortium as a whole nor the individual partners that implicitly or explicitly participated in the creation and publication of this document shall be liable or responsible, in negligence or otherwise, for any loss, damage or expense whatever sustained by any person as a result of the use, in any manner or form, of any knowledge, information or data contained in this document, or due to any inaccuracy, omission or error therein contained.




**Funded by
the European Union**

Public Summary

This deliverable, “Project management handbook” provides a comprehensive description of the management strategy to be followed in the project such as management tools, the risk management approach, and progress monitoring and quality assurance procedures, to guarantee that its outcomes meet the planned objectives and reach high implementation quality.

The project coordinator (FM) is in charge of scientific coordination, quality assurance and risk management of the project.

The project manager (I2M) provides management guidelines to the partners on project level. The project partners – in particular WP leaders - are responsible for the management at WP level, securing good progress, good collaboration and compliance to the Description of Action (DoA).

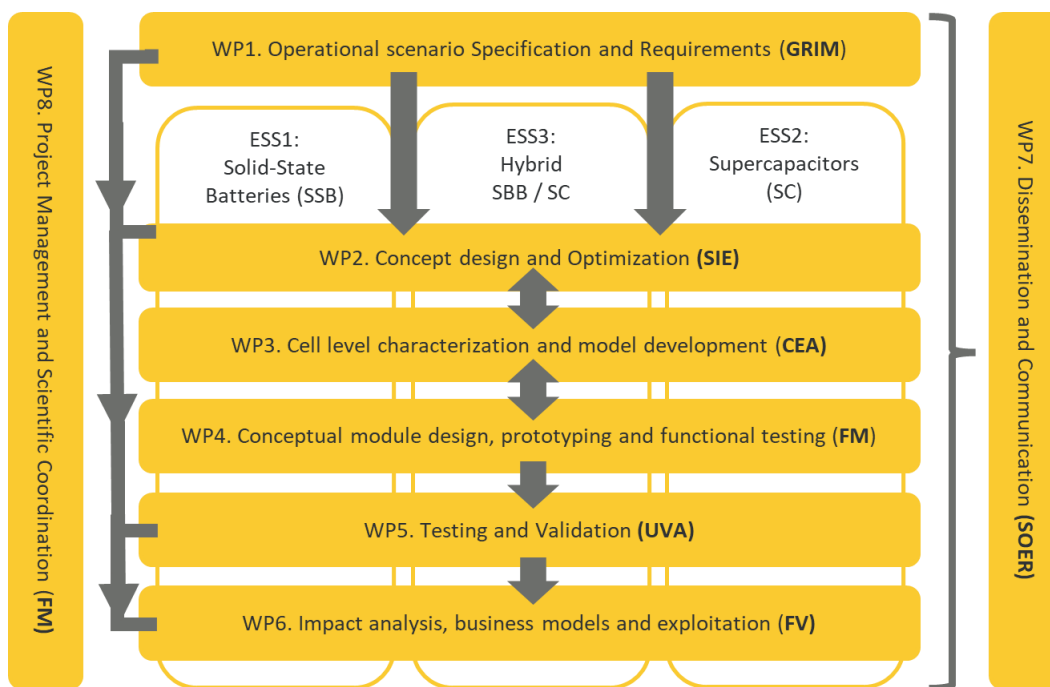

Below an overview of the WP structure and WP leaders.
